

COQUILLE INDIAN TRIBE

KILKICH TRANSPORTATION SAFETY PROJECT Weekly Update• May 26, 2023



CONSTRUCTION ACTIVITIES

The Kilkich Transportation Safety Project has kicked off with contractor mobilization, setting up the site boundaries, environmental protection, safety signage, and bringing in heavy and light equipment.

WHAT TO EXPECT NEXT WEEK


Construction activities next week begin with the closure of the Kilkich Administration Building parking lot on Tuesday, May 30th. See reverse for alternate parking instructions on this day. Knife River will also begin stripping the wooded debris from the bogs on the 30th. This work will continue during workdays, until June 6th.

ENVIRONMENTAL PROTECTION EFFORTS

Knife River has installed BMPs in the Miluk/Mexeye construction area. A BMP is a method used to prevent or control stormwater runoff and the discharge of pollutants, including sediment, into local waterbodies. For this phase, that includes perimeter silt fences and storm drain inlet protection.


SIGN UP FOR UPDATES

We strongly encourage you to sign up for Construction Updates through <u>Nixle!</u> TEXT keyword "BUILD" to 888777. Updates will be provided weekly throughout the project.

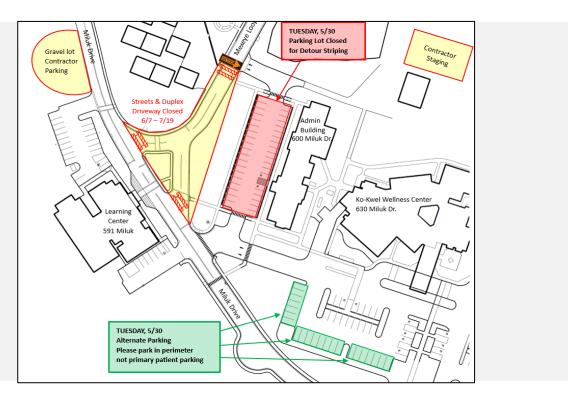

PARKING CHANGES

Tuesday, May 30th, the Kilkich Administration Building parking lot will be closed to install temporary road striping for the traffic detour route. Please plan to park in the perimeter parking at the Ko-Kwel Wellness Center. Please <u>do not</u> park in the primary patient parking areas. Parking in the Administrative Parking lot will reopen Wednesday, May 31st.

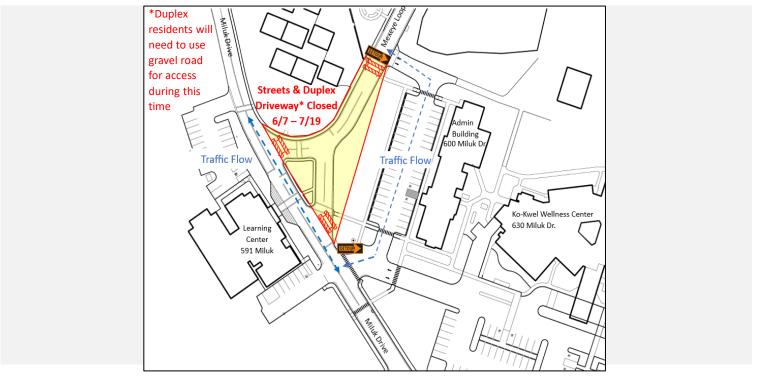

ROAD CLOSURES & DETOURS

Beginning June 7th, Mexeye Loop will be closed in the area highlighted in yellow above. The road is expected to reopen July 19th. Barricades will be installed, and a detour will be in place. The detour will guide traffic off Miluk/Mexeye through the Kilkich Administration Building parking lot. The detour is expected to be in place through late July.
