



# COQUILLE INDIAN TRIBE

## KILKICH TRANSPORTATION SAFETY PROJECT Weekly Update • June 9, 2023



### CONSTRUCTION ACTIVITIES

The bog work is complete. The areas have been cleaned up and the contractor is using space for their equipment and materials.

Excavation of Mexeye Loop started this week. The contractor has saw cut and removed the asphalt and new utility lines have been installed crossing the roadway. These utilities will feed future growth in the bogs. This growth will be identified during the master planning process, coming soon.


Beginning today, Friday, June 9<sup>th</sup>, a portion of the grassy area in front of the Kilkich Administration Building and the “triangle” planter in the center of the roadway are being excavated in preparation of the rerouted roadway.

### WHAT TO EXPECT NEXT WEEK

Construction activities will continue with excavation and removal of the grassy and planter areas. You will see sidewalks and curbs in the construction area also excavated and removed to prepare for the new layout. Street light poles in the construction zone will also be removed to prepare for relocation and new lighting.

## ENVIRONMENTAL PROTECTION EFFORTS

The environmental controls are being monitored throughout each day. The roadways will be swept and cleaned each Friday before the weekends.

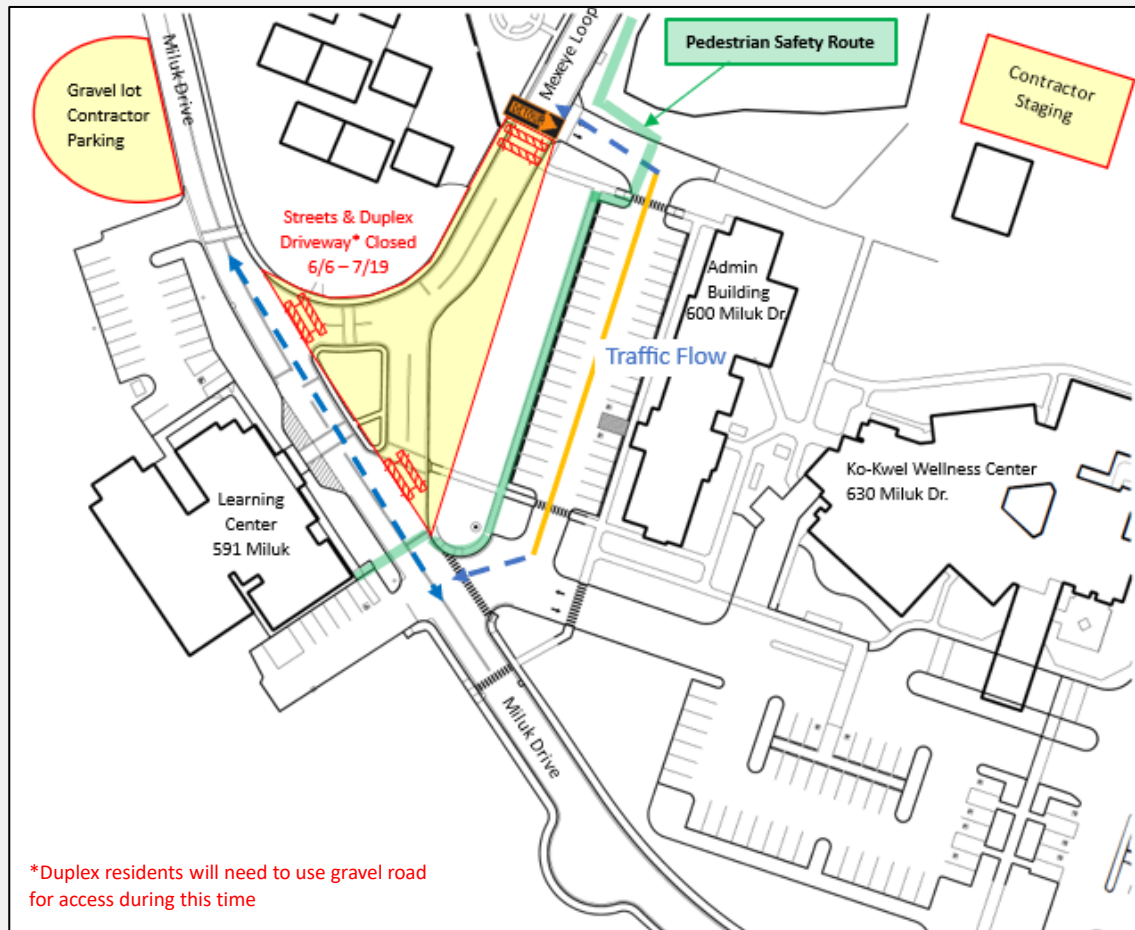

## ROAD CLOSURES & DETOURS

Beginning June 5<sup>th</sup>, Mexeye Loop was closed in the area highlighted in yellow above. The road is expected to reopen July 19<sup>th</sup>. Barricades are installed and a detour is in place. The detour guides traffic off Miluk Drive/Mexeye Loop through the Kilkich Administration Building parking lot.

Above is an updated map that includes a pedestrian safety route. This route will be in effect through this phase of the project. The pedestrian route is near the construction zone so please take care while utilizing it.







## PROGRESS PHOTOS:

Knife River removing the grassy and planter areas and newly excavated roadways.

## SIGN UP FOR UPDATES

We strongly encourage you to sign up for Construction Updates through [Nixle!](#) TEXT keyword "BUILD" to 888777. Updates will be provided weekly throughout the project.



## WANT MORE?

Interested in more photos? Want to see past updates? Check out the "Projects" tab on the Coquille Indian Tribe website.

