



COQUILLE INDIAN TRIBE

KILKICH TRANSPORTATION SAFETY PROJECT Weekly Update • June 16, 2023



CONSTRUCTION ACTIVITIES

Excavation of Mexeye Loop continued this week; sidewalks, curbs, the grassy area in front of the Kilkich Administration Building and much of the “triangle” planter were removed. Utilities were installed parallel to the roadway and rock is being graded and compacted to prepare for road base.


WHAT TO EXPECT NEXT WEEK

Roadway work will continue through the week. The concrete curb, sidewalk, and driveway forms will be prepared and set. Street light poles in the construction zone will also be removed to prepare for relocation and new lighting with light bases installed towards the end of the week.

ENVIRONMENTAL PROTECTION EFFORTS

The environmental controls are being monitored throughout each day. The roadways will be swept and cleaned each Friday before the weekends.

The eaglets at 4th Creek Reservoir are growing fast! They are being monitored thanks to a combination of NRO staff and their Eagle Watch program as well as the Learning Center kids monitoring the nest each week.

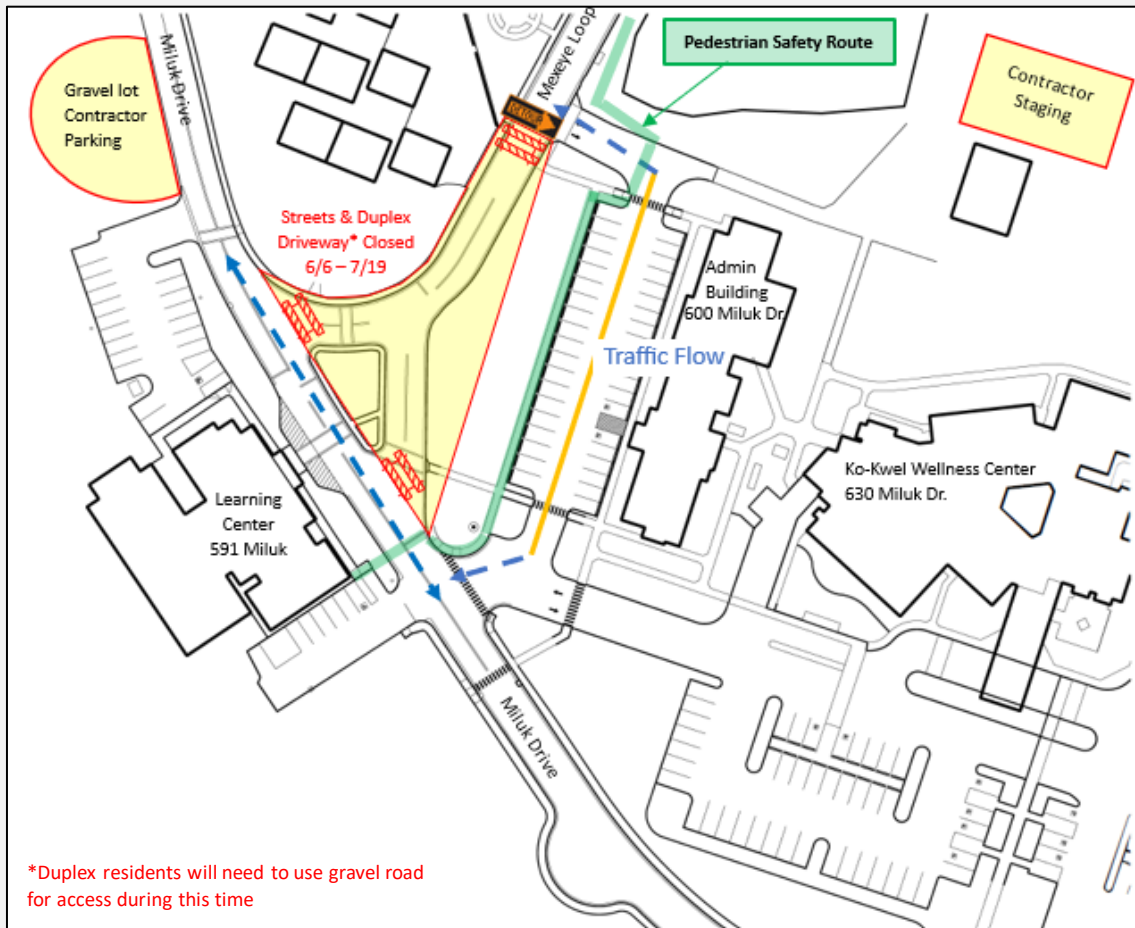

ROAD CLOSURES & DETOURS

Beginning June 5th, Mexeye Loop was closed in the area highlighted in yellow above. The road is expected to reopen July 19th.

Barricades are installed and a detour is in place. The detour guides traffic off Miluk Drive/Mexeye Loop through the Kilkich Administration Building parking lot.

Please see the map above for vehicular and pedestrian routes. Please use caution when using all detour routes.



SIGN UP FOR UPDATES

We strongly encourage you to sign up for Construction Updates through [Nixle](#)! TEXT keyword "BUILD" to 888777. Updates will be provided weekly throughout the project.



PROGRESS PHOTOS:

Knife River excavating and grading the roadway. Newly prepped sidewalk areas and utility installation.



WANT MORE?

Interested in more photos? Want to see past updates? Check out the "Projects" tab on the Coquille Indian Tribe website.

