



COQUILLE INDIAN TRIBE

KILKICH TRANSPORTATION SAFETY PROJECT Weekly Update • June 30, 2023



CONSTRUCTION ACTIVITIES

Things are shaping up on Mexeye Loop. The concrete curbs, gutters, sidewalk, and driveway forms were set, and some have been poured. The hillside in front of the Kilkich Admin building has been cut back and new paths have been cut in preparation of ADA sidewalks. Street light poles in the construction zone have been removed to prepare for relocation.

As mentioned in last week's alert, we have skipped ahead and begun some excavation work in the Learning Center parking lot. This work was originally part of Phase 3, but due to a delay caused by fiber utility contractors, workflow had to be rearranged to keep the project on schedule.

The current excavation work will be contained in the existing parking lot and avoid the gravel lot to the west until the two little eaglets have fledged the nest which is expected to happen in August.




WHAT TO EXPECT NEXT WEEK

In observance of the holiday next week, the contractor will not be working Monday, July 3rd & Tuesday, July 4th. Work next week will focus on preparing the existing Learning Center parking lot for asphalt and setting some of the concrete forms for the sidewalks, gutters, and driveway.

ENVIRONMENTAL PROTECTION EFFORTS

The environmental controls are being monitored throughout each day by the contractor, PMO and NRO staff. The roadways will be swept and cleaned each Friday before the weekend.

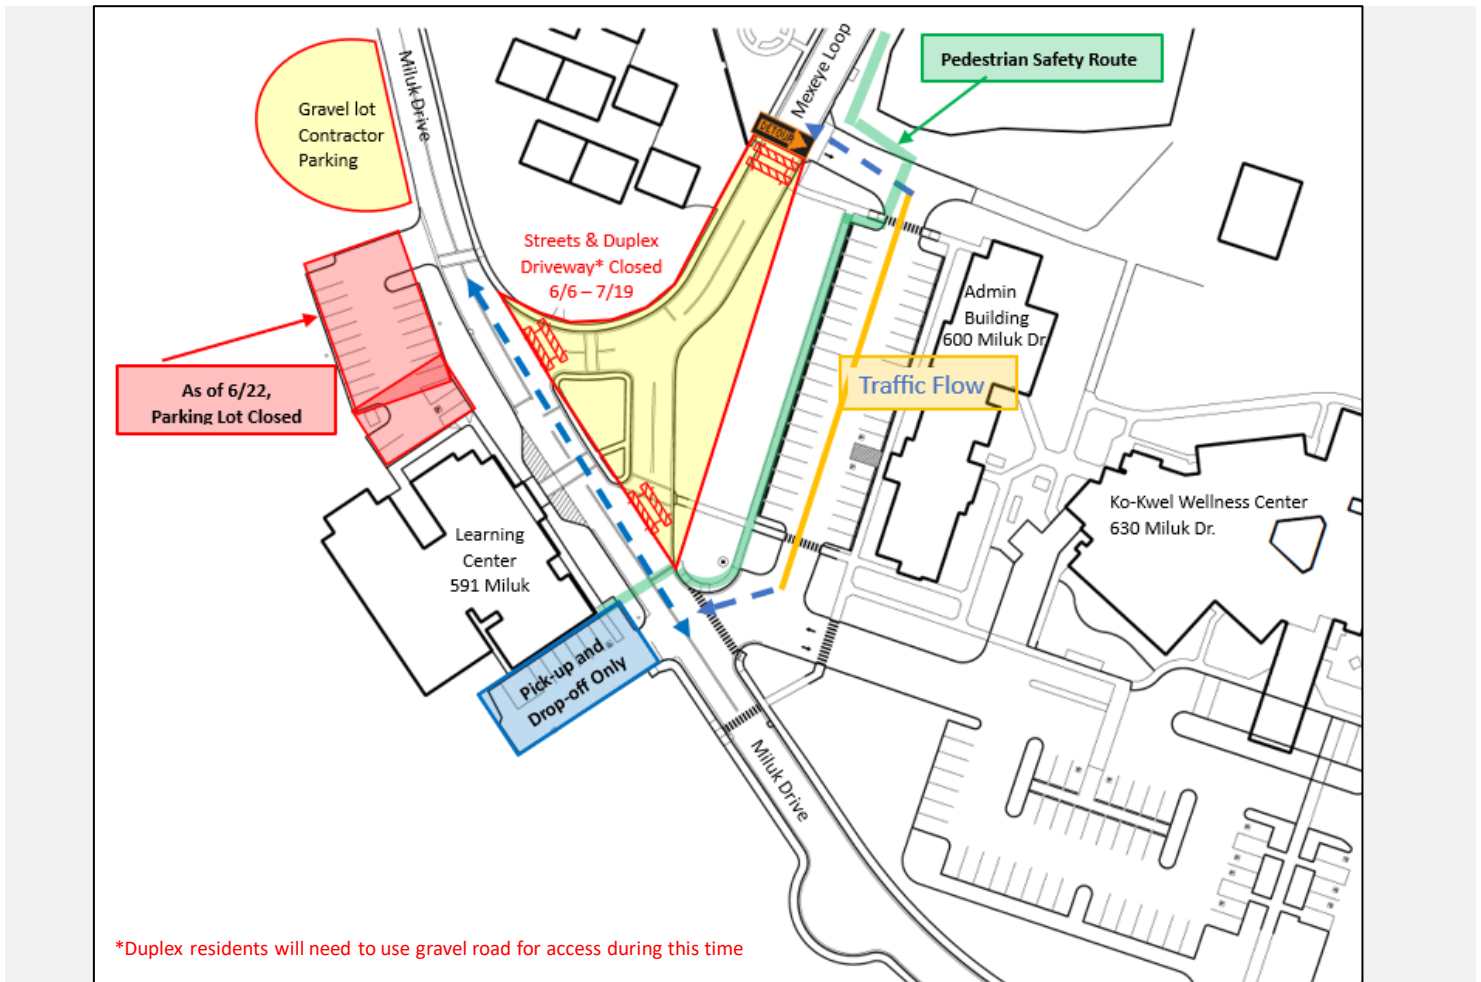

ROAD CLOSURES & DETOURS

Beginning June 5th, Mexeye Loop was closed in the area highlighted in yellow above. The road is expected to reopen July 19th. Barricades are installed and a detour is in place. The detour guides traffic off Miluk Drive/Mexeye Loop through the Kilkich Administration Building parking lot.

The parking lot to the west of the Learning Center (in red) is closed as of June 22nd. The parking lot to the east of the Learning Center (in blue) will be for student pick-up and drop-off only. All staff and visitors that need to park longer than 15 minutes, please utilize parking across the street in the KWC parking lot

PROGRESS PHOTOS:

Knife River & Brock Construction finishing curbs, gutters, sidewalks, and driveway. Kyle Electric installing conduit in preparation for new lighting.

SIGN UP FOR UPDATES

We strongly encourage you to sign up for Construction Updates through [Nixle](#)! TEXT keyword "BUILD" to 888777. Updates will be provided weekly throughout the project.



WANT MORE?

Interested in more photos? Want to see past updates? Check out the "Projects" tab on the Coquille Indian Tribe website.

