



# COQUILLE INDIAN TRIBE

## KILKICH TRANSPORTATION SAFETY PROJECT Weekly Update • August 4, 2023



### CONSTRUCTION ACTIVITIES

Things were rearranged a little bit this week as site conditions caused some slight design changes. Instead of what was previously planned, the Learning Center parking lot was completely excavated, and road and curb work continued near the building. The driveway at the duplexes was saw cut and excavated to prepare for a new slope design and asphalt. The curbs near the flagpole were removed to prepare for new sidewalks, curbs, and gutters.


### WHAT TO EXPECT NEXT WEEK

New curbs, gutters, sidewalks, and ADA ramps will be formed and prepped for new concrete. Towards the end of the week, these forms will be poured and finished. Rock will be installed on the new roadway and in the Learning Center parking lot in preparation of the new asphalt.

There will be several activities that cause flagging and traffic delays next week. An area of the temporary road will be sawcut and removed to set a new vault lid for the Ziplly Fiber vault. A temporary "bump" will be in place here until the last layers of asphalt are finished. The existing "old" road, west of the new roadway on Miluk Drive, will be removed and rebuilt all the way back to the Learning Center parking lot entrance. Please see "Road Closures and Detours" for more information and a map of activities.

## ENVIRONMENTAL PROTECTION EFFORTS

The environmental controls are being monitored throughout each day by the contractor, PMO and NRO staff. The roadways will be swept and cleaned each Friday before the weekend. No new news on the eaglet.

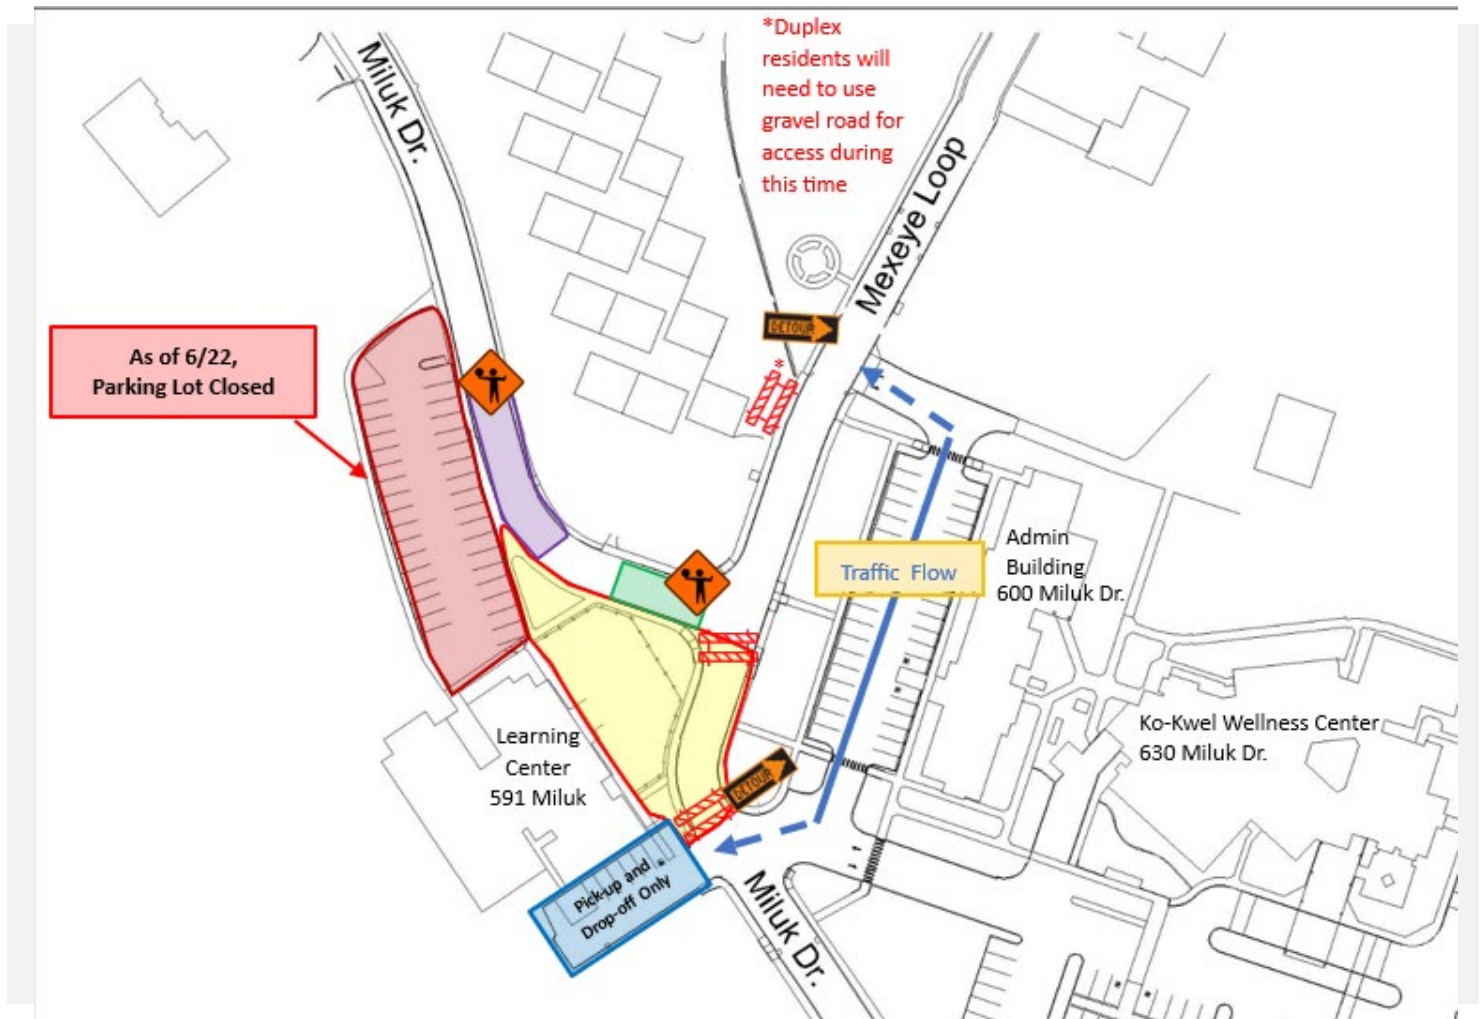

## ROAD CLOSURES & DETOURS

This will be a very busy week for traffic changes. The Phase 2 detour is in place in the area of Miluk Drive, highlighted in yellow above. The detour guides traffic off Miluk Drive onto Mexeye Loop and through the Killich Administration Building parking lot and back onto Miluk Drive.

On Monday, August 7<sup>th</sup>, between 8am and 4pm, flaggers will be in place for the new Ziply vault lid to be installed, noted in green above. On Thursday and Friday, August 10<sup>th</sup> and 11<sup>th</sup>, from 7am-5pm, flaggers will be in place to remove and rebuild the roadway noted in purple above. Traffic will be delayed 10-15 minutes in both directions during these dates and times.

The parking lot to the west of the Learning Center (in red) will remain closed. The parking lot to the east of the Learning Center (in blue) will be for student pick-up and drop-off only.

All staff and visitors that need to park longer than 15 minutes, please utilize parking across the street in the KWC parking lot.





### **PROGRESS PHOTOS:**

Excavation of duplex driveway, Learning Center parking lot, and Miluk Drive.

### **SIGN UP FOR UPDATES**

We strongly encourage you to sign up for Construction Updates through Nixle! **TEXT** keyword "BUILD" to 888777. Updates will be provided weekly throughout the project.



### **WANT MORE?**

Interested in more photos? Want to see past updates? Check out the "Projects" tab on the Coquille Indian Tribe website.

