



# COQUILLE INDIAN TRIBE

## KILKICH TRANSPORTATION SAFETY PROJECT Weekly Update • August 11, 2023



### CONSTRUCTION ACTIVITIES

Whew! We made it through the week of traffic delays and flagging. The new Ziplly Fiber vault lid was successfully installed in the roadway. The existing “old” road, west of the new roadway on Miluk Drive to the Learning Center parking lot was quickly removed and rocked in one day. The began forming new curbs, gutters, sidewalks, and ADA ramps in both the roadway and the parking lot.

### WHAT TO EXPECT NEXT WEEK


Brock Construction will continue work on the new curbs, gutters, sidewalks, and ADA ramps around the roadway and in the parking lot. These will be poured mid next week.

The main priority next week is to get to work regrading the Learning Center parking lot in preparation for school starting soon. The courtyard in front of the building is also a top priority. The new retaining wall/fence footing will begin layout and construction. New topsoil will be placed in preparation for hydroseeding towards the end of the project in a more supportive growing climate.

## ENVIRONMENTAL PROTECTION EFFORTS

The environmental controls are being monitored throughout each day by the contractor, PMO and NRO staff. The roadways will be swept and cleaned each Friday before the weekend.

According to NRO, the eaglets have fledged! Look to the skies for a chance to see them.

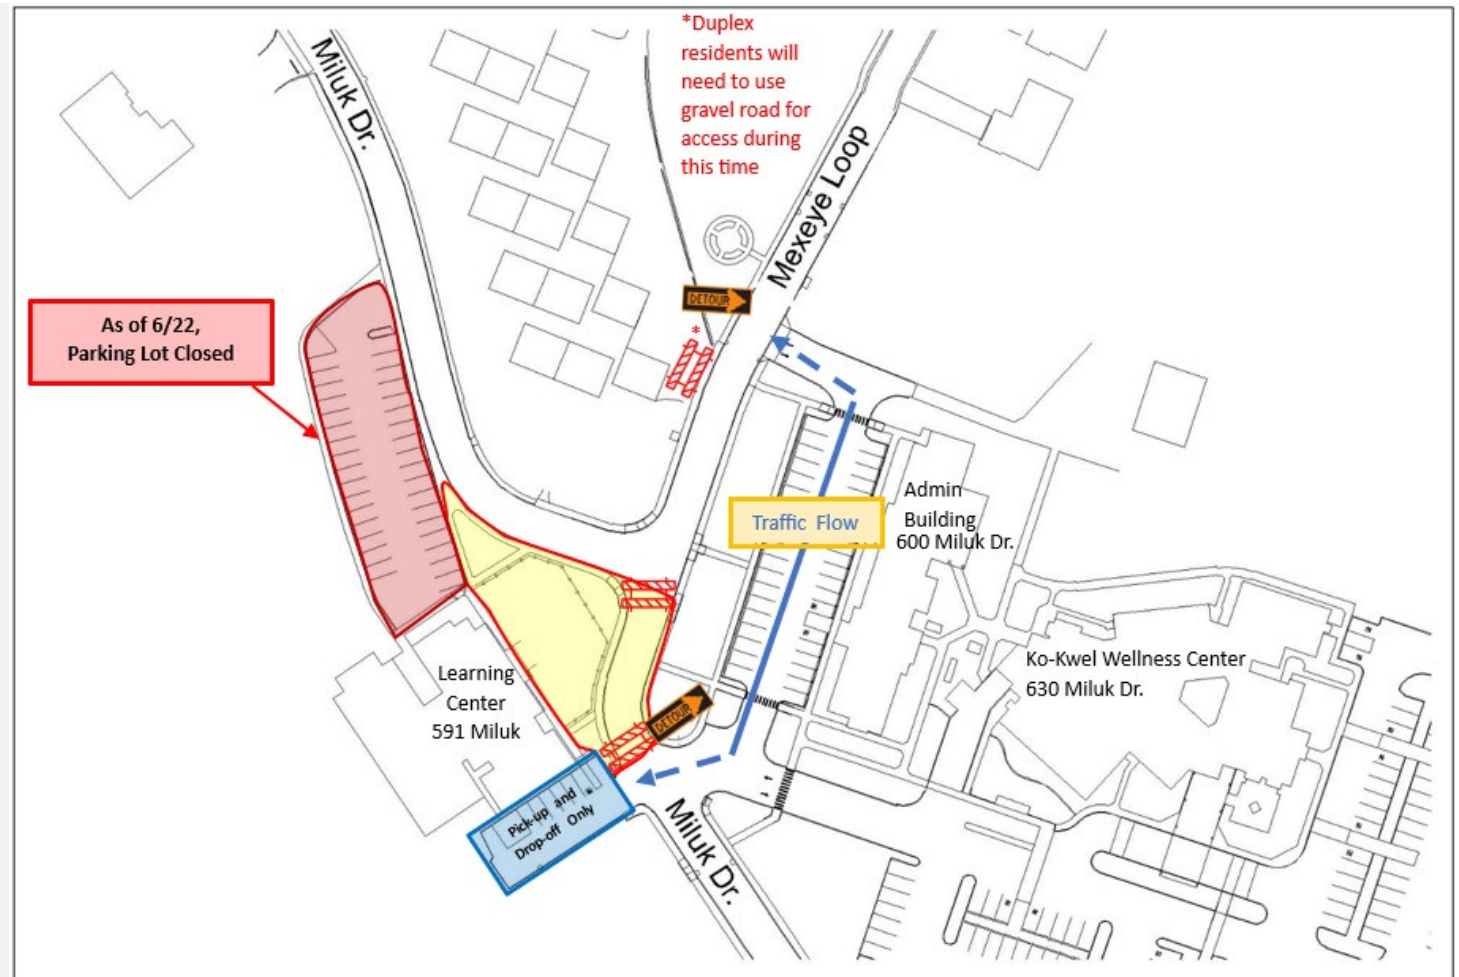

## ROAD CLOSURES & DETOURS

We are back to the Phase 2 detour with no additional impacts this week. The detour guides traffic off Miluk Drive onto Mexeye Loop and through the Killich Administration Building parking lot and back onto Miluk Drive.

The parking lot to the west of the Learning Center (in red) will remain closed. The parking lot to the east of the Learning Center (in blue) will be for student pick-up and drop-off only.

All staff and visitors that need to park longer than 15 minutes, please utilize parking across the street in the KWC parking lot.



## PROGRESS PHOTOS:

Learning Center  
Courtyard and parking  
lot, newly formed  
intersection.



## SIGN UP FOR UPDATES

We strongly encourage you to sign up for Construction Updates through [Nixle!](#) TEXT keyword "BUILD" to 888777. Updates will be provided weekly throughout the project.

## WANT MORE?

Interested in more photos?  
Want to see past updates?  
Check out the "Projects" tab on  
the Coquille Indian Tribe  
website.

