



COQUILLE INDIAN TRIBE

KILKICH TRANSPORTATION SAFETY PROJECT Weekly Update • September 8, 2023



CONSTRUCTION ACTIVITIES


Sidewalks, curbs, and gutter work continued throughout the project. Work on the new fence footing and courtyard layout continued. The new topsoil for the courtyard was also delivered. Work is continuing west down the road to add new sidewalks towards the CELS building and extending the existing sidewalk down to the highway.

WHAT TO EXPECT NEXT WEEK

Brock Construction will continue work on the new curbs, gutters, sidewalks, and ADA ramps around the roadway and in the parking lot. The footings for the new courtyard fence will be formed. Kyle Electric will be installing new light poles.

ENVIRONMENTAL PROTECTION EFFORTS

The environmental controls are being monitored throughout each day by the contractor, PMO and NRO staff. The roadways are swept and cleaned each Friday before the weekend.

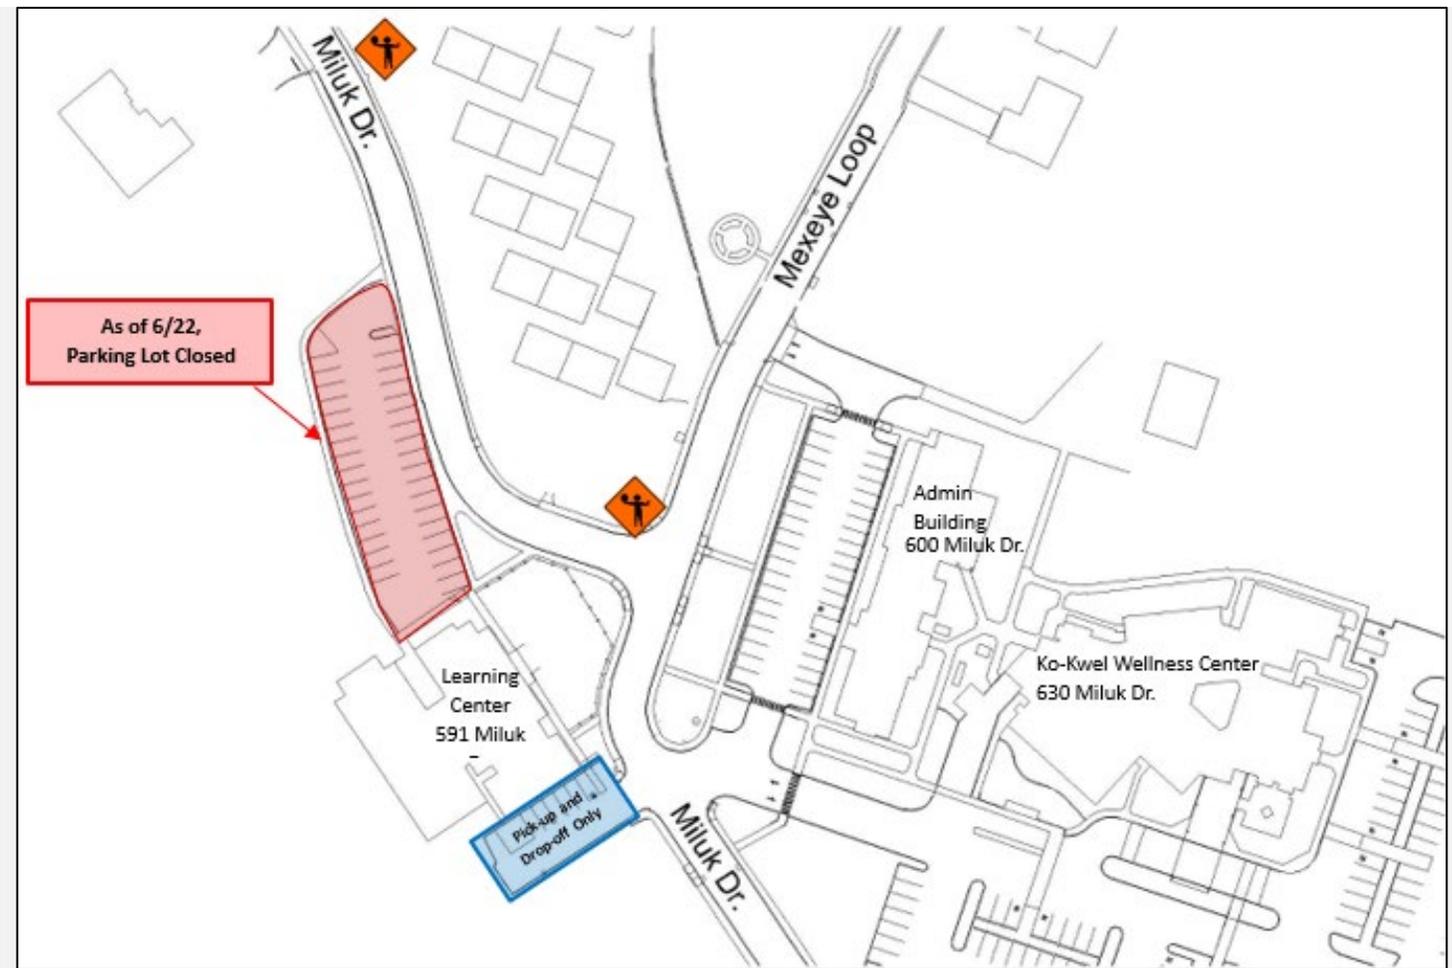

ROAD CLOSURES & DETOURS

With the new asphalt base lift on Miluk Drive, the roads will be open whenever possible. There will be intermittent closures whenever work needs to be done in the new Miluk Drive area.

We will see flaggers continuously through the next few weeks to keep workers safe, as new sidewalk, curbs, and gutter work continues down Miluk Drive.

The parking lot to the west of the Learning Center (in red) will remain closed for a couple more weeks with hopes of reopening by September 22nd. The parking lot to the east of the Learning Center (in blue) will be for student pick-up and drop-off only.

All staff and visitors that need to park longer than 15 minutes, please utilize parking across the street in the KWC parking lot.



PROGRESS PHOTOS:

Concrete work in the Learning Center parking lot, Learning Center Courtyard with topsoil delivery

WANT MORE?

Interested in more photos? Want to see past updates? Check out the "Projects" tab on the Coquille Indian Tribe website.



SIGN UP FOR UPDATES

We strongly encourage you to sign up for Construction Updates through [Nixle!](#)

TEXT keyword "BUILD" to 888777.

Updates will be provided weekly throughout the project.

