



COQUILLE INDIAN TRIBE

KILKICH TRANSPORTATION SAFETY PROJECT Weekly Update • October 6, 2023



CONSTRUCTION ACTIVITIES

Happy October. The project is almost done! Phew, what a busy week! Monday and Tuesday, the roads received the final layer of asphalt. The grass area in front of the Kilkich Administration Building was graded in preparation for hydroseeding. Some of the sidewalks in front of the building were demolished to prepare for the new ADA sidewalk tie-in. Work continued with new sidewalks, curbs, and gutters down Miluk Drive. The new gravel road driveway approach was poured and will cure over the weekend.

WHAT TO EXPECT NEXT WEEK (and the following)

Due to staff availability, there will be no update sent out next week. We are going to attempt to capture what is coming in the next two weeks in this update. Please note, as weather changes, things may shift.


In the next two weeks will see the finish of the installation of the communication lines near the Kilkich Administration Building, for new construction. The entry into the parking lot toward the Cranberry bogs will be widened slightly during the process. Work will continue in front of the Learning Center for the new courtyard and down Miluk Drive finishing up the sidewalks, curbs, gutters, and new roadway.

ENVIRONMENTAL PROTECTION EFFORTS


The environmental controls are being monitored throughout each day by the contractor, PMO and NRO staff. The roadways are swept and cleaned each Friday before the weekend. New BMPs will be added near the Kilkich Administration Building as work for communication and power installation occurs.

ROAD CLOSURES & DETOURS

Demo and reconstruction of the gravel road driveway approach, adjacent sidewalk, and asphalt began on Monday, 9/18. The driveway will be poured today, Friday, October 6th and will cure over the weekend. We anticipate the gravel road reopening towards the end of next week. Until reopening, this area will be completely blocked off until fully finished. Duplex residents will need to use the exit onto Mexeye Loop. Road closed signs will be posted near the duplex driveway entrance.

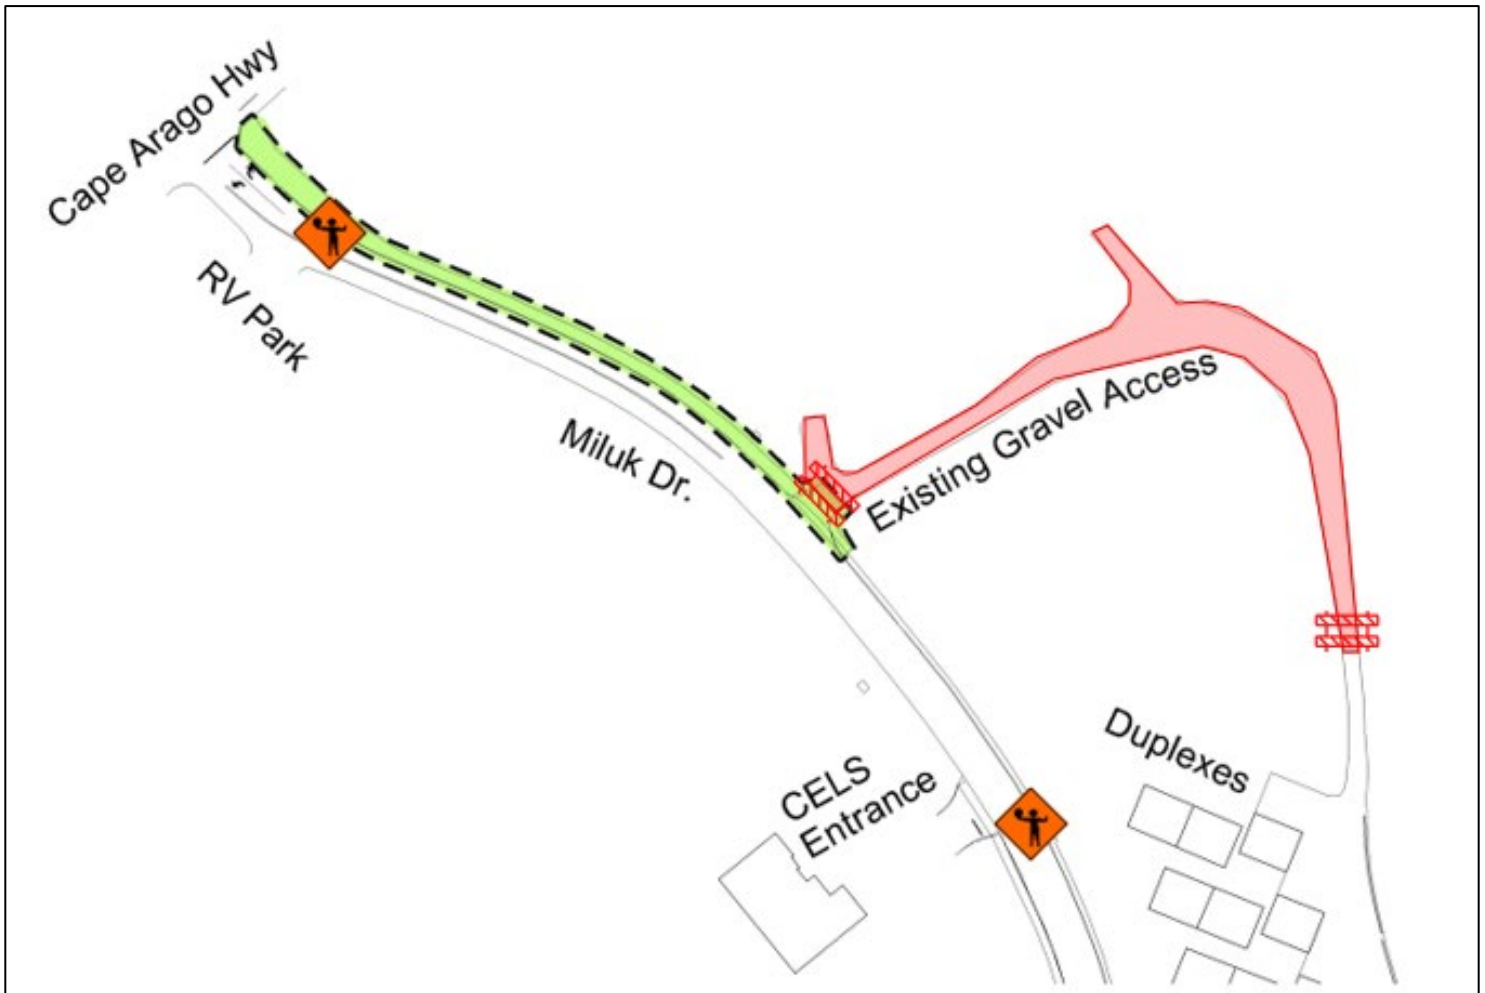

ROAD CLOSURES & DETOURS, cont.

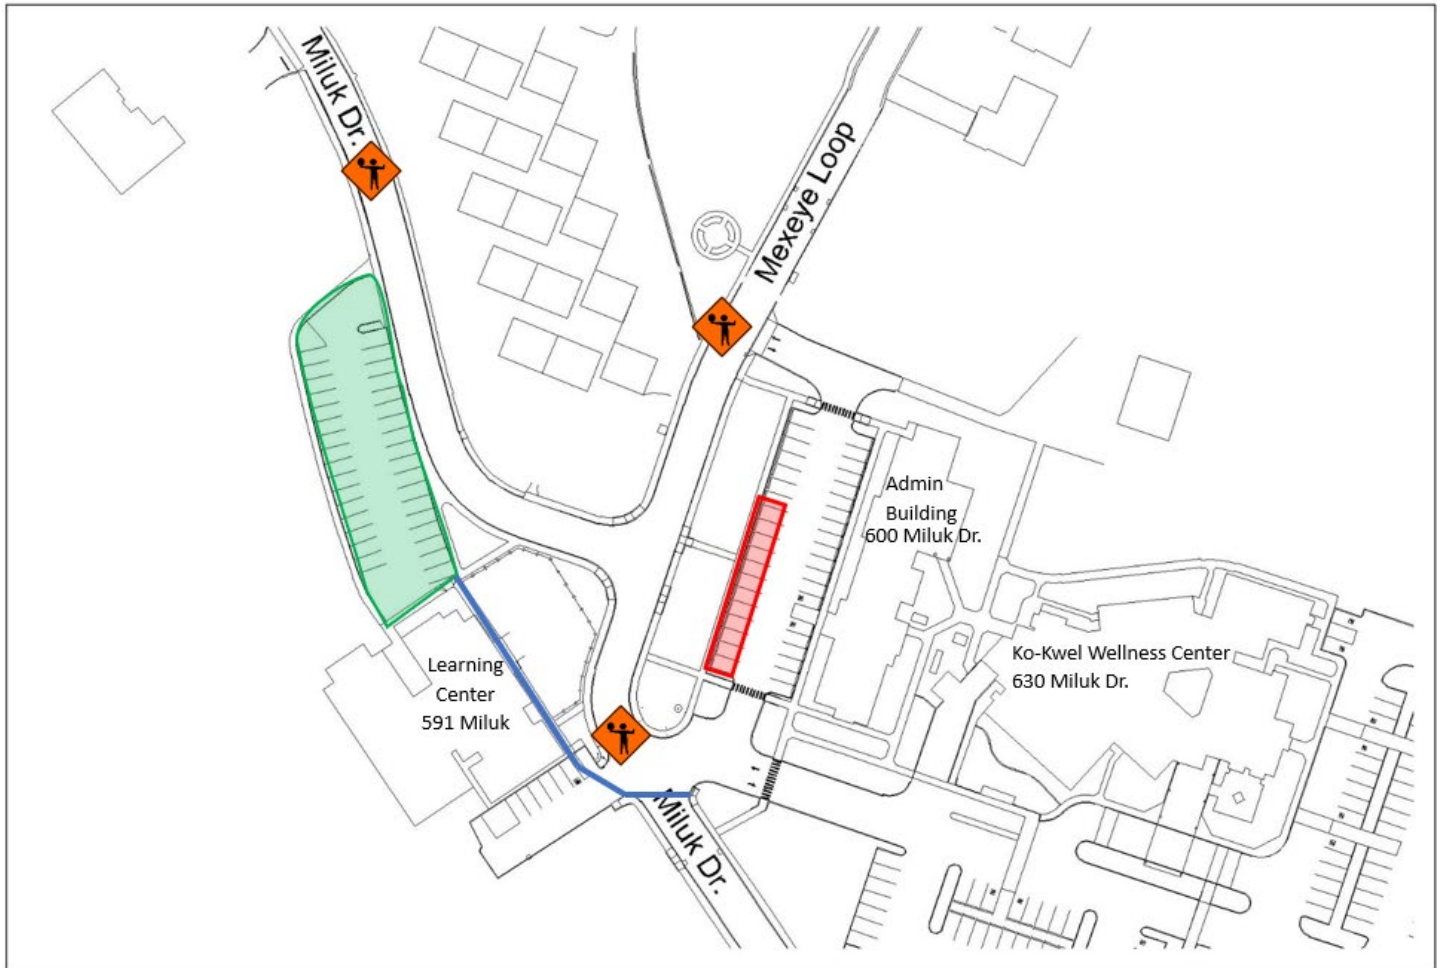

Parking in front of the Killich Administration Building will be reduced next week, as shown above, while work on the new ADA sidewalks is completed. Please plan to park in the new Learning Center parking lot as an overflow and use the pedestrian path (in blue above) to access the sidewalks across Miluk Drive.

We will see flaggers continuously through the next few weeks to keep workers safe, as new sidewalk, curbs, and gutter work continues down Miluk Drive.

The new Shishda Haws project will be breaking ground next week in the east side of the Ko-Kwel Wellness Center parking lot. Please watch for a separate update with parking impacts related to that project.



PROGRESS PHOTOS:

Grading and ADA sidewalk near in the Kilkich Administration Building. New curbs, gutters, and formed sidewalks heading up Miluk Drive.

SIGN UP FOR UPDATES

We strongly encourage you to sign up for Construction Updates through [Nixle](#)! TEXT keyword "BUILD" to 888777.

WANT MORE?

Interested in more photos? Want to see past updates? Check out the "Projects" tab on the Coquille Indian Tribe website.

