



COQUILLE INDIAN TRIBE

KILKICH TRANSPORTATION SAFETY PROJECT Weekly Update • September 15, 2023



CONSTRUCTION ACTIVITIES

Sidewalks, curbs, and gutter work continued throughout the project. Work on the new fence footing and courtyard layout continued. Work continued west down the road to add new sidewalks towards the CELS building and extending the existing sidewalk down to the highway. Most exciting is the Learning Center parking lot received asphalt! Striping will be completed next week, and the lot will be useable as of Monday, September 25th.

WHAT TO EXPECT NEXT WEEK


The Learning Center parking lot will be completed and ready for use. The driveway approach on the gravel road to the duplexes will be formed and prepped for concrete. See "Road Closures & Detours" for impact information. Brock Construction will continue work on the new curbs, gutters, sidewalks, and ADA ramps down the roadway. The footings for the new courtyard fence will be formed. Kyle Electric will be installing new light poles.

ENVIRONMENTAL PROTECTION EFFORTS


The environmental controls are being monitored throughout each day by the contractor, PMO and NRO staff. The roadways are swept and cleaned each Friday before the weekend.

ROAD CLOSURES & DETOURS

Demo and reconstruction of the gravel road driveway approach, adjacent sidewalk, and asphalt will begin on Monday, 9/18 with an expected completion for reopening on Friday, 9/29. This area will be completely blocked off until fully finished. Duplex residents will need to use the exit onto Mexeye Loop. Road closed signs will be posted near the duplex driveway entrance.

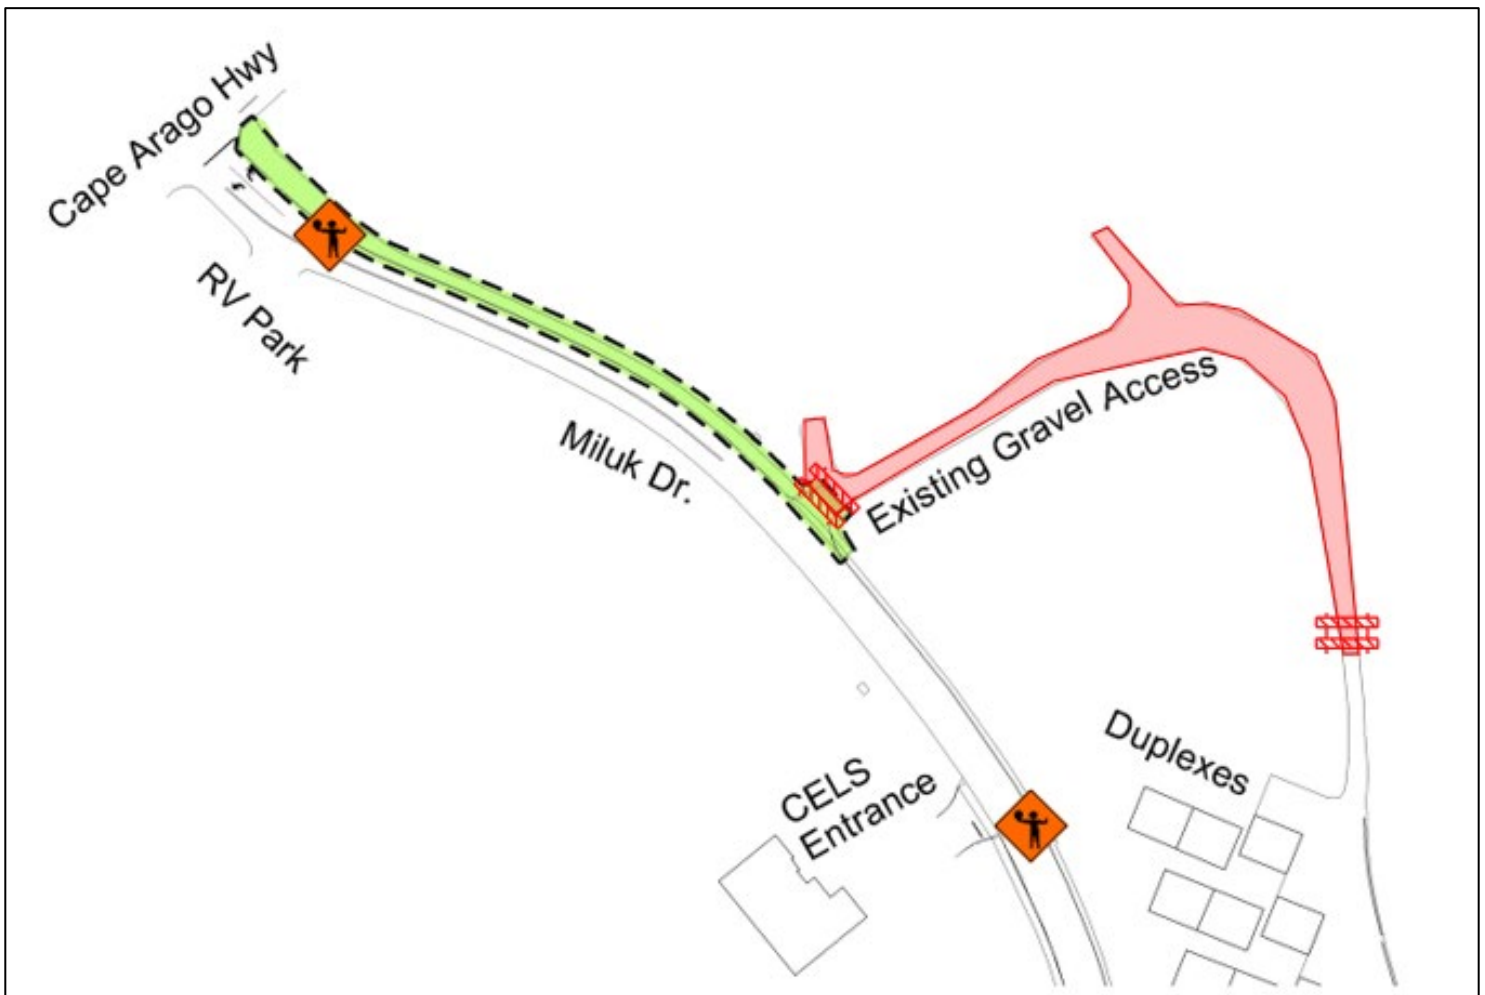

ROAD CLOSURES & DETOURS, CONT.

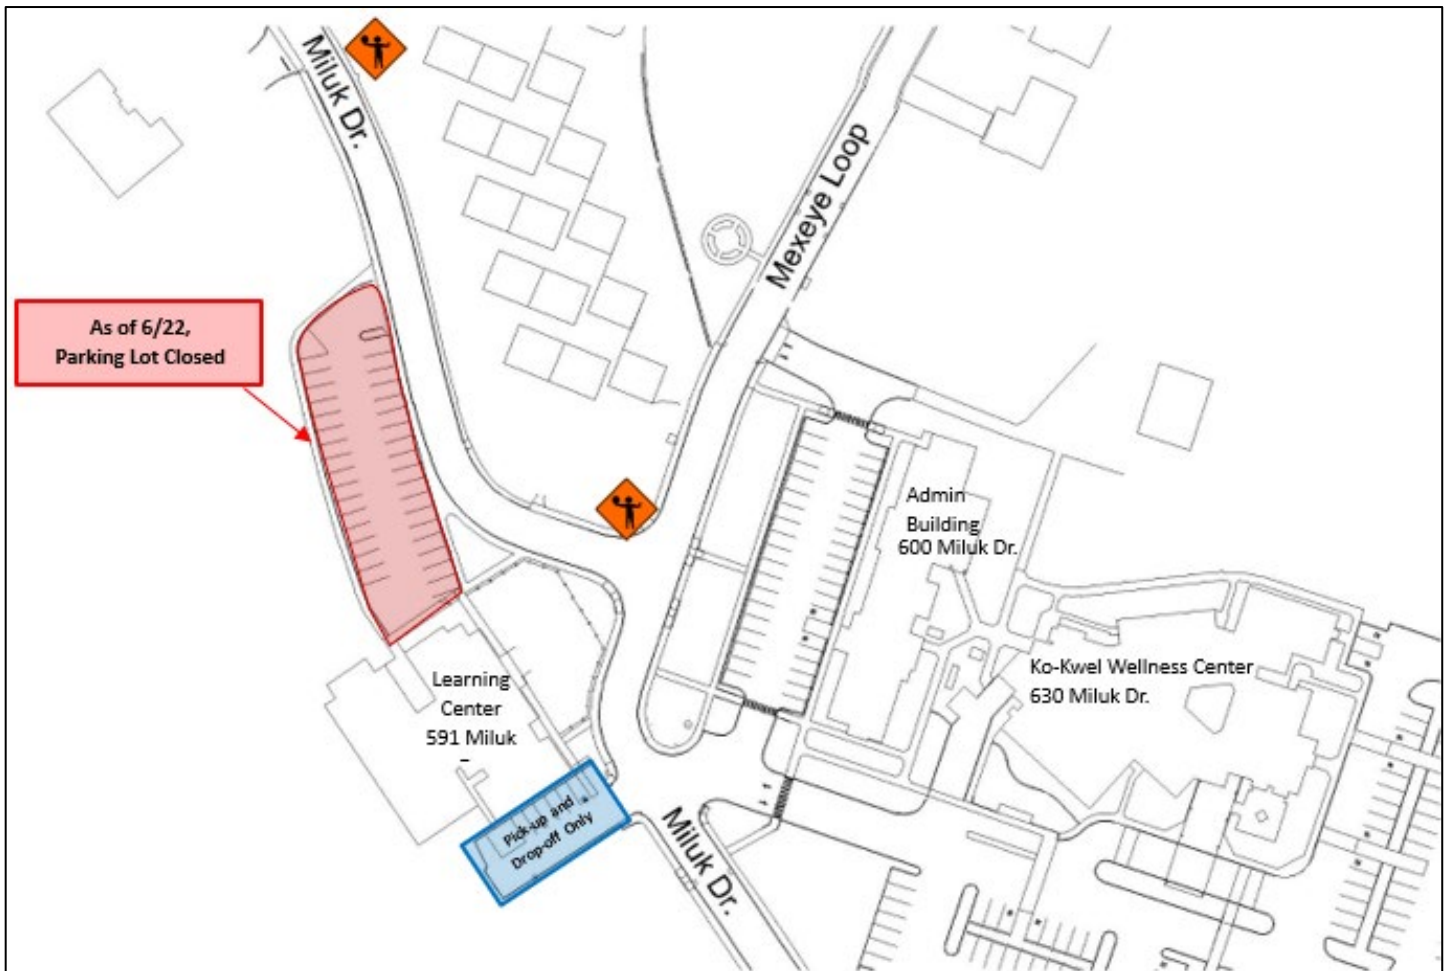

With the new asphalt base lift on Miluk Drive, the new roads will be open whenever possible. There will be intermittent closures whenever work needs to be done in the new Miluk Drive area.

We will see flaggers continuously through the next few weeks to keep workers safe, as new sidewalk, curbs, and gutter work continues down Miluk Drive.

The parking lot to the west of the Learning Center (in red) will remain closed for a one more week. The parking lot to the east of the Learning Center (in blue) will be for student pick-up and drop-off only. All staff and visitors that need to park longer than 15 minutes, please utilize parking across the street in the KWC parking lot.



WANT MORE?

Interested in more photos? Want to see past updates? Check out the "Projects" tab on the Coquille Indian Tribe website.



PROGRESS PHOTOS:

Paving work in the Learning Center parking lot, Learning Center Courtyard new sidewalk forms

SIGN UP FOR UPDATES

We strongly encourage you to sign up for Construction Updates through [Nixle!](#)
TEXT keyword "BUILD" to 888777.

