




# COQUILLE INDIAN TRIBE

## KILKICH TRANSPORTATION SAFETY PROJECT Weekly Update • September 28, 2023

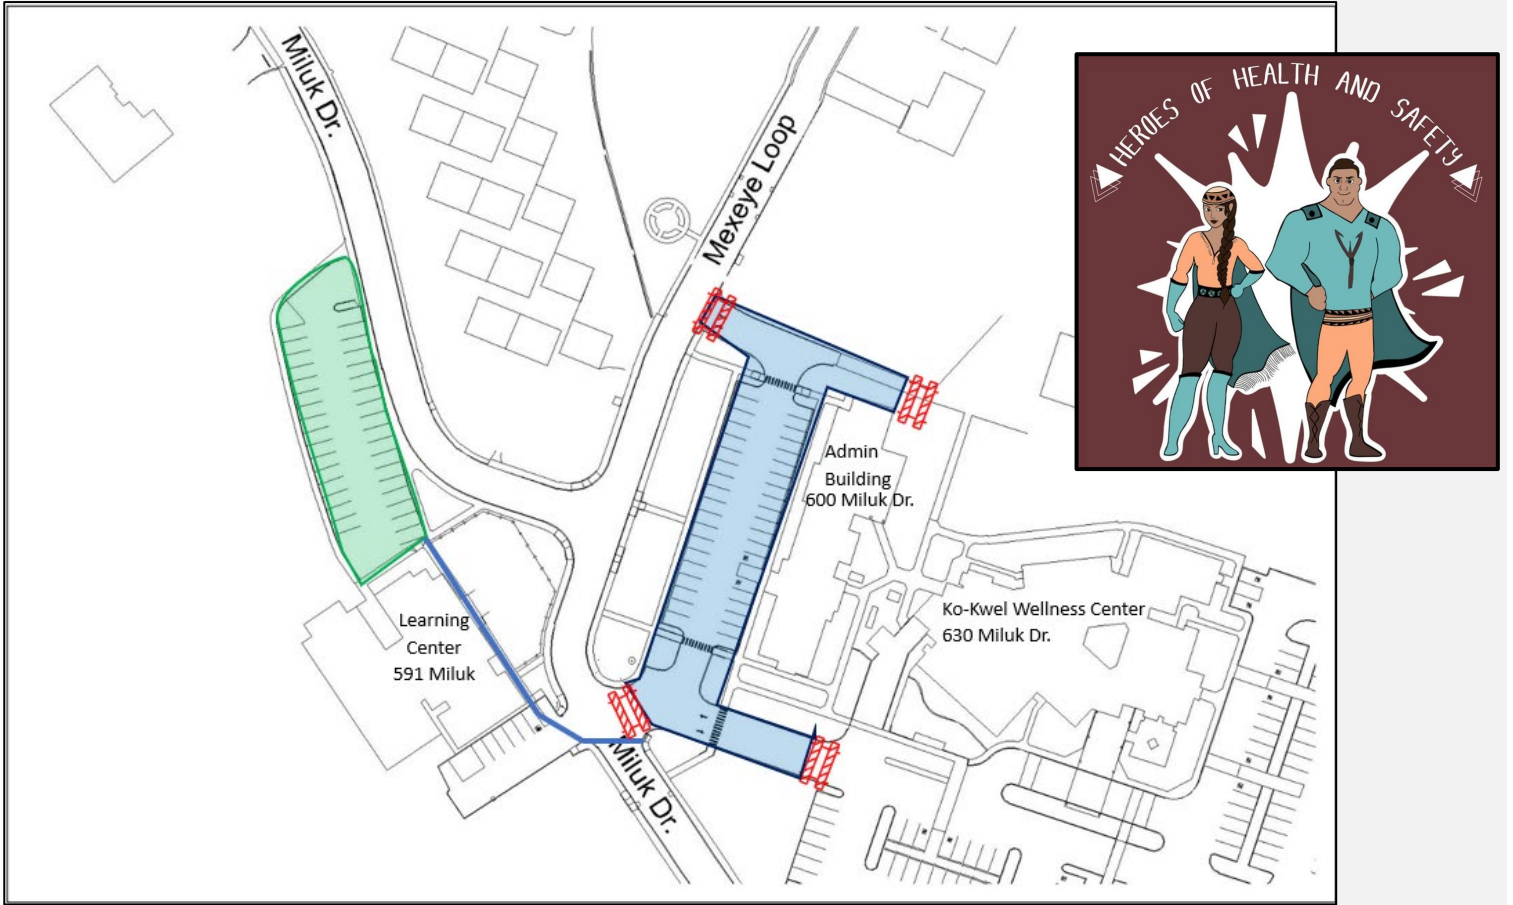

### **SAFETY FAIR & BIKE BONANZA PARKING IMPACTS**

We wanted to start this week's update with a reminder about tomorrow's event and provide information about the parking impacts that the event will have.

"Heroes of Health and Safety" is the theme of this year's Safety Fair and Bike Bonanza that is coming up on Friday. The event will take place outside of the Ko-Kwel Wellness Center, in front of the Kilkich Administration Building, on Friday, Sept. 29, from 3:30 to 6 PM. There will be food, games, prizes, health and safety education coordinated by Community Services and, of course, fun!

This is open to Tribal members, Kilkich residents, Head Start families, and CIT/KWC staff.

The Kilkich Administration Building parking lot will be closed to vehicles all day on Friday. Please plan to park in the new Learning Center parking lot (in green). Please utilize the pedestrian path (in blue) to access the event safely.

## CONSTRUCTION ACTIVITIES

Sidewalks, curbs, and gutter work continued down Miluk Drive with the new driveway approach at the gravel road being formed and ready for concrete. Work on the new fence footing and courtyard layout continued. Work continued west down the road to add new sidewalks towards the CELS building and extending the existing sidewalk down to the highway.



## WHAT TO EXPECT NEXT WEEK


Next week will be a little crazy! Monday and Tuesday, the roads will receive the final layer of asphalt. The grass area in front of the Kilkich Administration Building will be graded in preparation for hydroseeding. The ADA sidewalks in front of the building will be completed. Work will continue on the Learning Center courtyard and the sidewalks/road down Miluk Drive. See "Road Closures & Detours" for impacts.

## ENVIRONMENTAL PROTECTION EFFORTS

The environmental controls are being monitored throughout each day by the contractor, PMO and NRO staff. The roadways are swept and cleaned each Friday before the weekend.


## ROAD CLOSURES & DETOURS

Demo and reconstruction of the gravel road driveway approach, adjacent sidewalk, and asphalt began on Monday, 9/18, with an expected completion for reopening on Friday, 9/29. This hit a bit of a weather delay and will continue to be closed for another week. This area will be completely blocked off until fully finished. Duplex residents will need to use the exit onto Mexeye Loop. Road closed signs will be posted near the duplex driveway entrance.

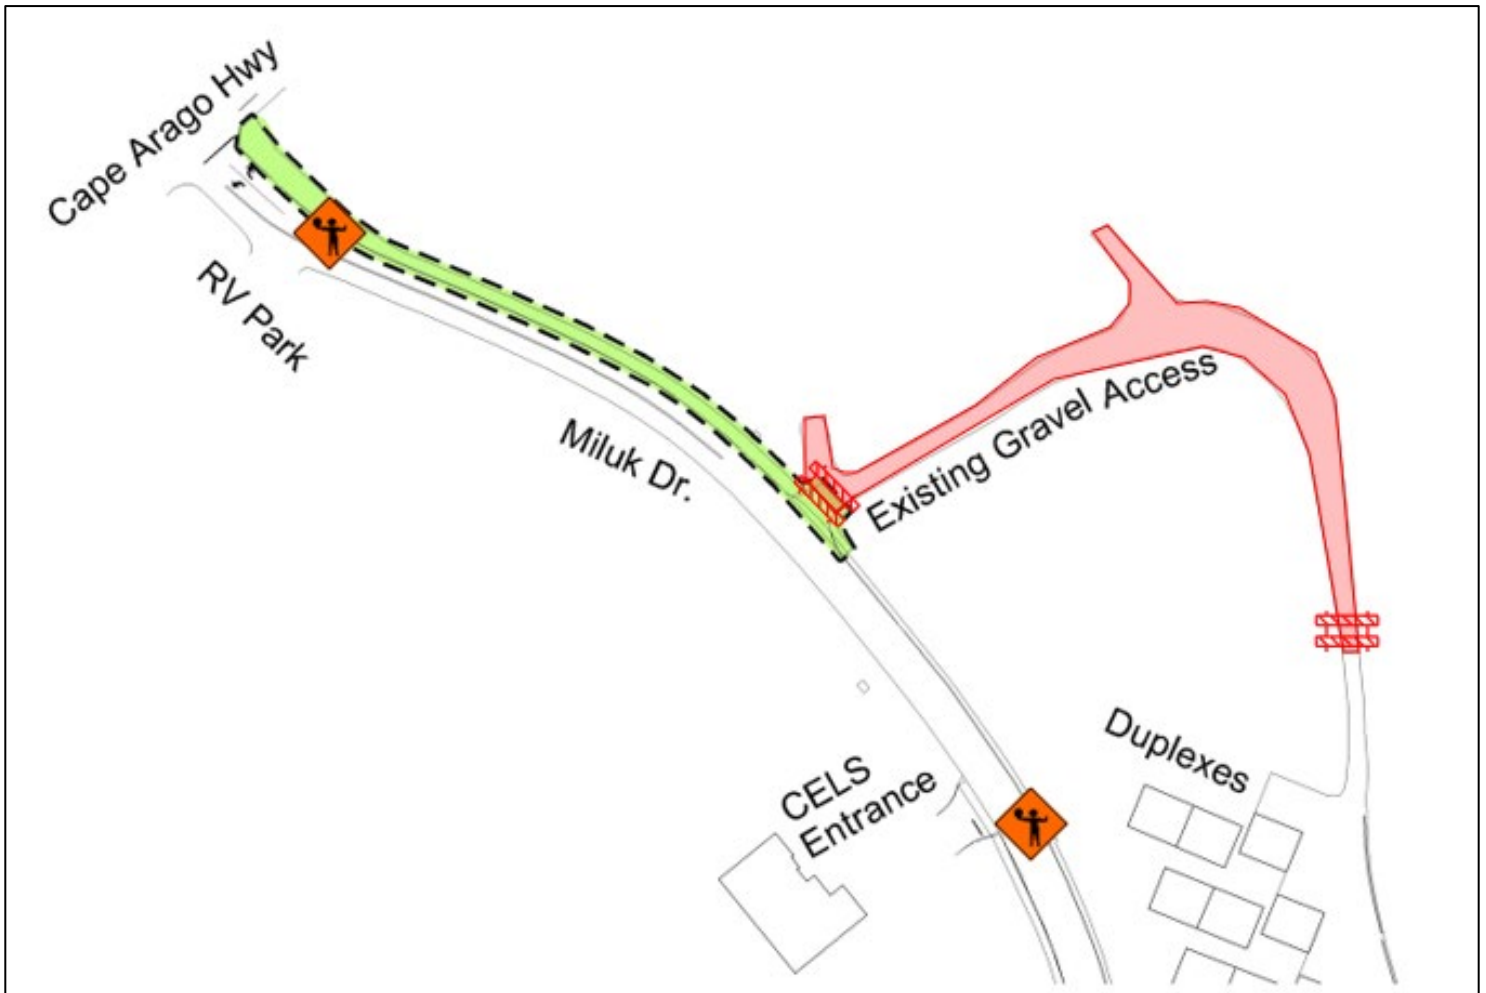

## ROAD CLOSURES & DETOURS, cont.

Installation of the final asphalt layer on the new intersection will cause extended delays with flagging on Monday and Tuesday, 10/2 & 10/3. Please plan for the extra time for travel.

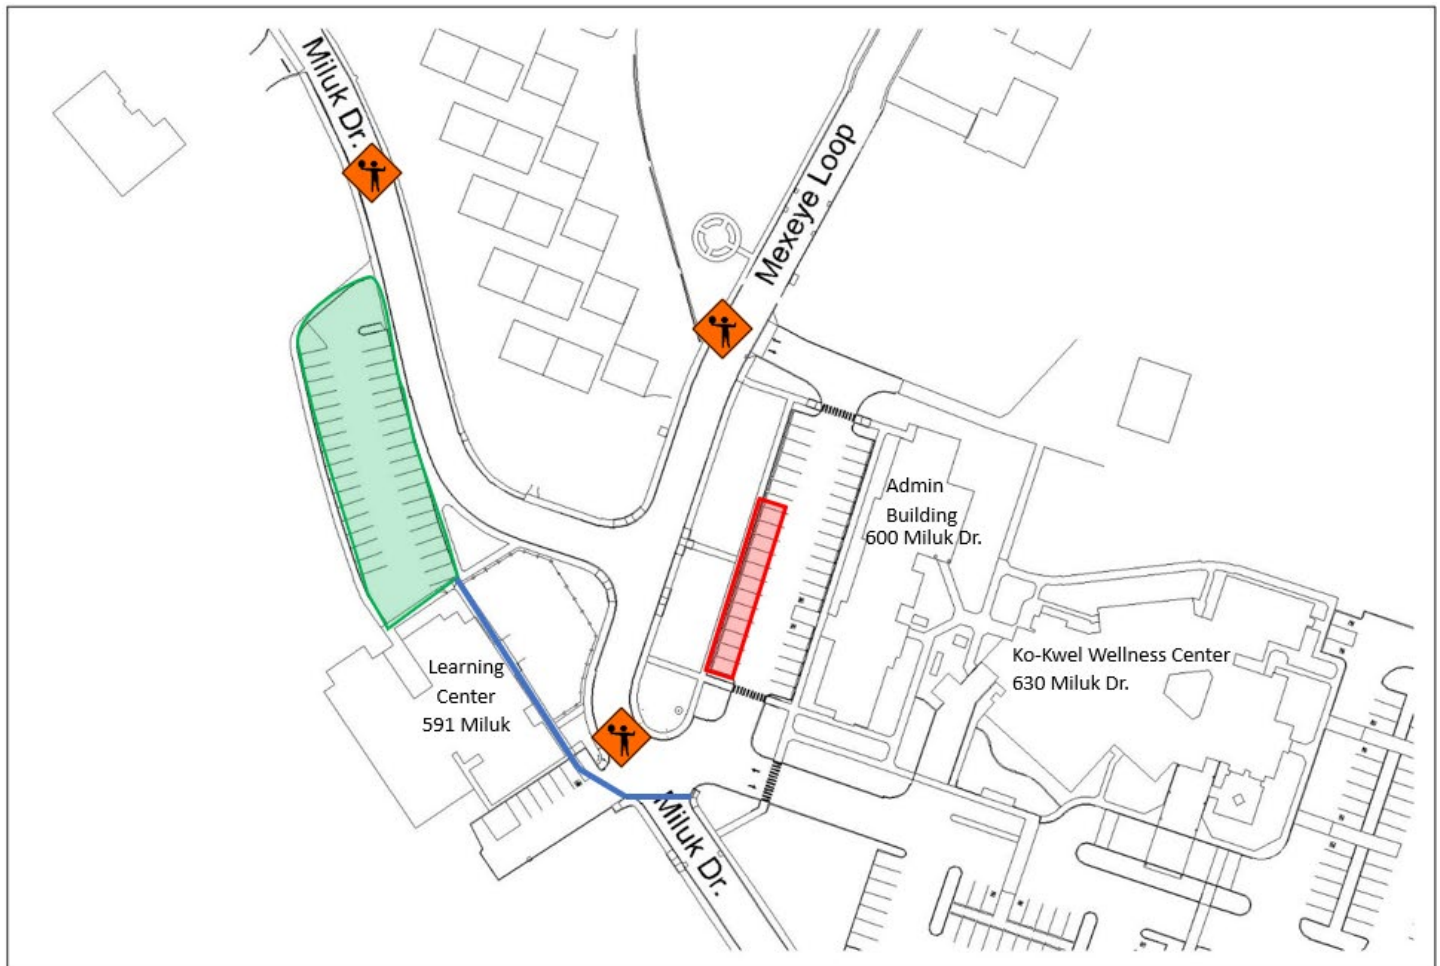

Parking in front of the Killich Administration Building will be reduced next week, as shown above, while work on the new ADA sidewalks is completed. Please plan to park in the new Learning Center parking lot as an overflow and use the pedestrian path (in blue above) to access the sidewalks across Miluk Drive.

We will see flaggers continuously through the next few weeks to keep workers safe, as new sidewalk, curbs, and gutter work continues down Miluk Drive.

The new Shishda Haws project will be breaking ground next week in the east side of the Ko-Kwel Wellness Center parking lot. Please watch for a separate update with parking impacts related to that project.



**PROGRESS PHOTOS:**  
New curbs, gutters, and formed sidewalks heading down Miluk Drive.

### **SIGN UP FOR UPDATES**

We strongly encourage you to sign up for Construction Updates through [Nixle!](#) TEXT keyword "BUILD" to 888777.

### **WANT MORE?**

Interested in more photos? Want to see past updates? Check out the "Projects" tab on the Coquille Indian Tribe website.

