



COQUILLE INDIAN TRIBE

KILKICH TRANSPORTATION SAFETY PROJECT Weekly Update • October 27, 2023



CONSTRUCTION ACTIVITIES

Road widening near the Kilkich Administration building was completed as well as the hydroseeding in front of the building. The cranberry bogs were also hydroseeded. The new fence footing for the Learning Center courtyard concrete was poured and topsoil work continued.

WHAT TO EXPECT NEXT WEEK

The Learning Center courtyard work will continue with the fence stem wall being formed and poured. The remaining sidewalk and curb work for the project will also be completed. Light pole work will be done in the Learning Center parking lot in preparation for the new poles.

FURTHER OUT

The project is mostly wrapped up next week with topsoil and hydroseeding of the remaining areas rounding out the following week. There are two longer lead items that will finish in the coming months. First, the new light poles for the Learning Center parking lot are still about five weeks out. The contractor will return once they are delivered to install them. The other long lead item is the fence that will be installed on top of the stem wall in the Learning Center courtyard. The fence should arrive for installation in early 2024.

ENVIRONMENTAL PROTECTION EFFORTS

The environmental controls are being monitored throughout each day by the contractor, PMO and NRO staff. The roadways are swept and cleaned each Friday before the weekend.

ROAD CLOSURES & DETOURS

On Monday, October 30th, Kyle Electric will be removing the existing light poles and bases in the Learning Center parking lot. Several spaces will be coned off for safety during this time. Please be cautious in the area during this time or make arrangements to park in another area.


Hopes are that the striping contractor has availability to finish the roadway striping. If they are able, there may be intermittent closures of the roadways during installation.

PROGRESS PHOTOS:

This page: Hydroseeding of the Killich Administration Building grassy area.

Next page: New sidewalks, curbs, and gutters up and down Miluk Drive near Cape Arago Highway.



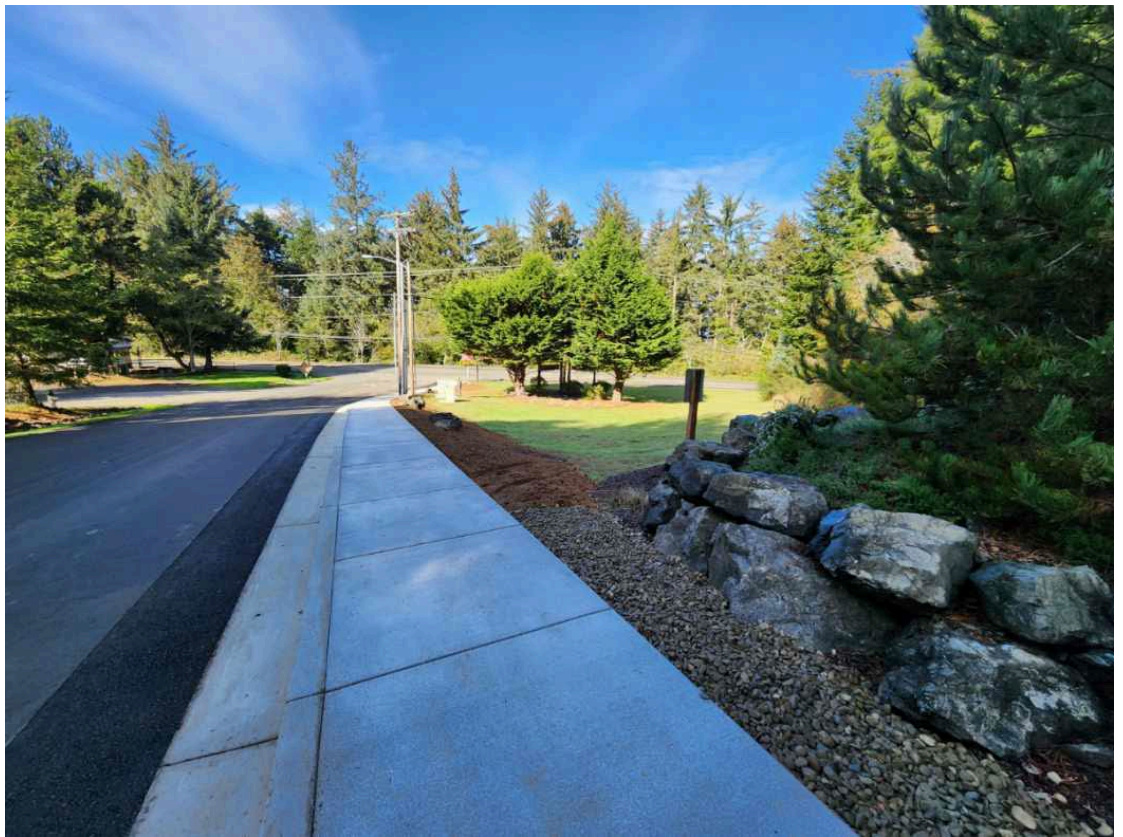

SIGN UP FOR UPDATES

We strongly encourage you to sign up for Construction Updates through [Nixle](#)!

TEXT keyword "BUILD" to 888777.

WANT MORE?

Interested in more photos? Want to see past updates? Check out the "Projects" tab on the Coquille Indian Tribe website.

