




### March Update

Weather has been a big factor in groundwork progress at the Shishda Haws site. We saw lots and lots of rain which forced a slight change of focus to dewatering the site instead of excavation. That system is now installed and drying things out nicely. Excavation and compaction can now move forward.

### Vibratory Rolling Impacts

**Monday, March 11<sup>th</sup> through Thursday, March 13<sup>th</sup>**, this work will require use of a vibratory compaction roller. **This will cause vibration to the surrounding buildings.**

## Ko-Kwel Wellness Center Main Parking Lot Entrance Closure

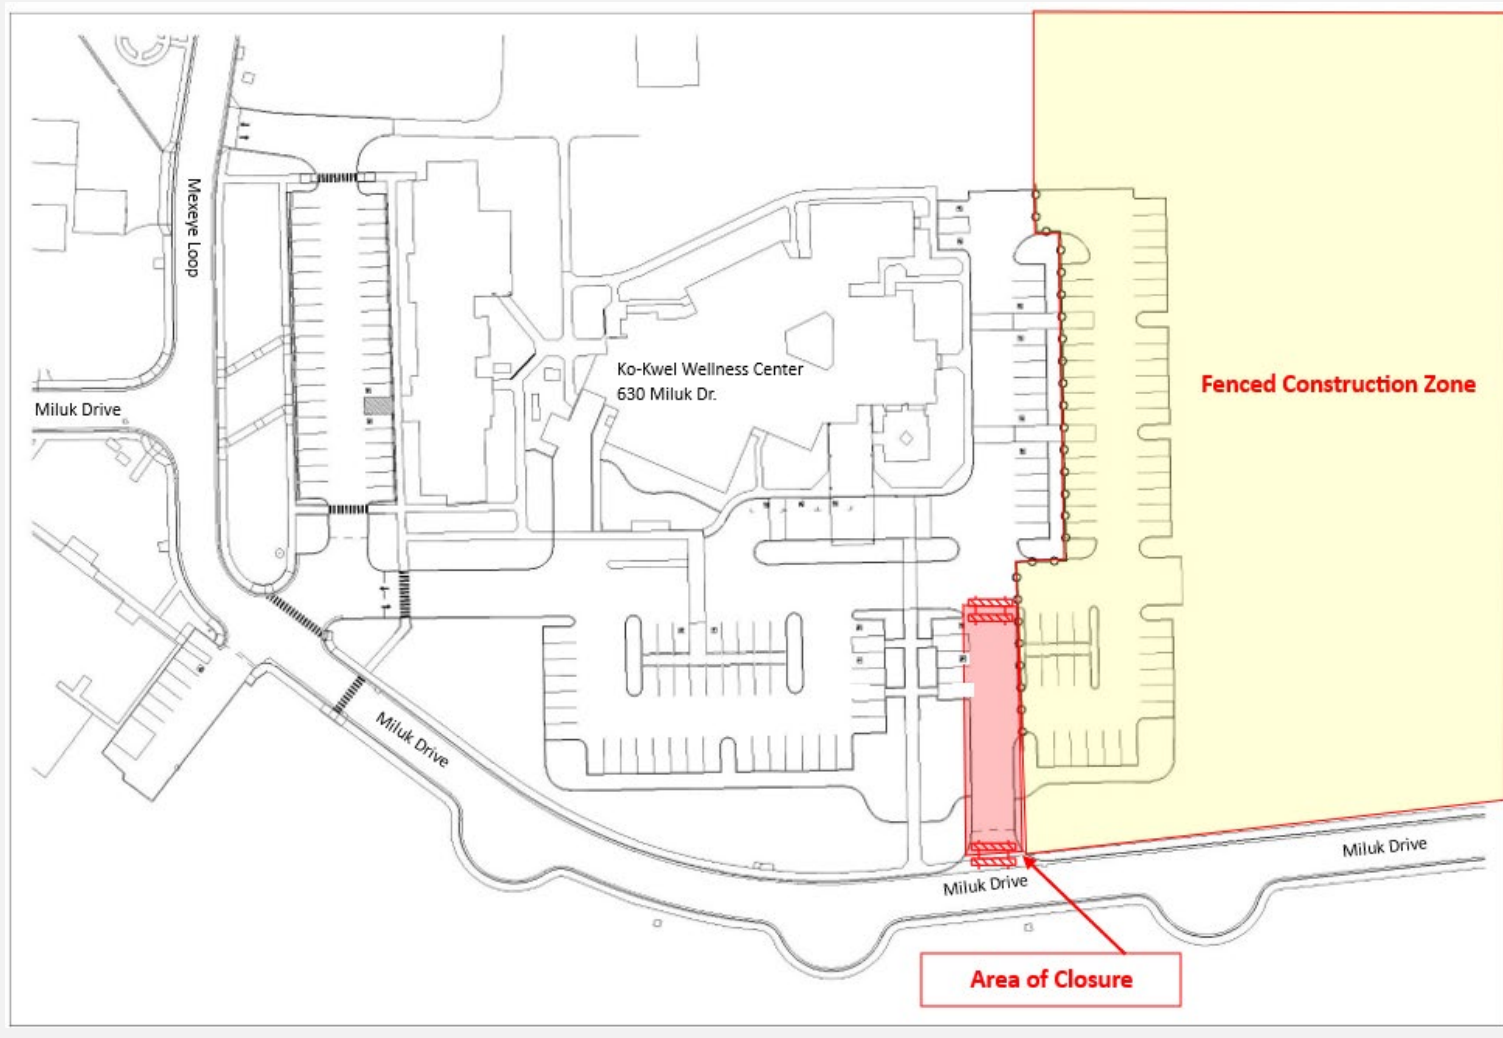

New utility connections are being installed for power, water, sewer, electrical, and internet. The first of these connections is the water and sewer lines. The construction for these will begin in early April. You will see trenching, pipe installation, and asphalt patching.

On **April 9<sup>th</sup>**, this work will extend across the **Ko-Kwel Wellness Center main parking lot entrance** causing a **closure (outlined above)**. The entrance will **reopen on April 13<sup>th</sup>**. The asphalt will be cut, the trench excavated, the pipe installed. The trench will then be filled, recompact, and covered with a temporary trench-plate (those big metal plates you sometimes see in road construction) in place until an asphalt patch can be completed.

Please use an alternate entrance during this time and always, please use caution near the construction area.



**Learn more**
